



深圳市诚锦鹏实业有限公司
SHENZHEN CHENGJINPENG INDUSTRIAL CO., LTD

无损检测报告

NONDESTRUCTIVE TESTING REPORT

工程名称 Project Name: PY4-2A 高压管线更换

High Pressure Manifold Replacement on PY4-2A Platform

委托单位 Commission Unit : 深圳市海基实业有限公司

委托单位地址 Client Address: 惠州市大亚湾石化大道中前兴
建材市场海基公司

工程编号 Project No. : CJP-WR-094-022-18-062

检测方法 Inspection Method : MT

报告编号 Report No. : CJP-WR-094-022-MT001-18-062

页数 Number of pages : 共 7 页

报告日期 Report Date : 2018.10.23

批准人 Approved by : 

检测单位: 深圳市诚锦鹏实业有限公司

CONTRACTOR: SHENZHEN CHENGJINPENG INDUSTRIAL CO.,LTD

地 址: 深圳市南山区月亮湾大道 2076 号高科大厦 6FC3

ADDRESS: C3F6, GAOKE BUILDING, NO.2076, YUELIANGWAN BLVD, NANSHAN DISTRICT, SHENZHEN

电 话 Tel: 0755-86274981/26440278

URL: <http://www.cjpsz.com> E-mail: cjpsz126@126.com



深圳市诚锦鹏实业有限公司

SHENZHEN CHENGJINPENG INDUSTRIAL CO., LTD

磁粉检测报告

MAGNETIC PARTICLE INSPECTION REPORT

项目名称:PY4-2A高压管线更换

报告日期

报告编号:

Project :High Pressure Manifold Replacement on PY4-2A Platform

Report Date: 2018.10.23

Report No.:CJP-WR-094-022-MT001-18-062

检测地点 Testing Position	PY4-2A平台	执行标准 Executive Standard	ASME B31.3	仪器型号 Instrument Type	ZCM-A2202	提升力 Lifting Power	≥45N		
检测比例 Testing Rate	--	合格级别 Acceptance Grade	--	仪器编号 Instrument No.	CJP-CF-22	磁粉 Magnetic Particle	MT-BW		
图纸号 Drawing No.	--	表面状态 Surface Condition	光滑 Smooth	磁轭类型 Yoke Type	AC-Yoke	反差剂 Contrast Agent	FA-5		
工件材质 Workpiece Material	30CrMo	灵敏度试块 Sensitivity block	A1(30/100)	磁化方法 Magnetizing Method	Successive	磁化时间 Magnetizing Time	1~3s		
工件编号 Workpiece No.	焊工号 Welder No.	焊口号 Weld No.	热处理状态 HTS	坡口形式 Groove Form	焊接方法 Welding Process	焊缝长度 W.L(mm)	缺陷编号 Defect No.	缺陷性质及大小 DNS	评定意见 Judge
PY4-2A-1	--	W14-1	--	V	GTAW	358	--	--	Acc
PY4-2A-2	--	W22-1	--	V	GTAW	358	--	--	Acc
PY4-2A-2	--	W25	--	V	GTAW	358	--	--	Acc
PY4-2A-3	--	W30-1	--	V	GTAW	270	--	--	Acc
PY4-2A-3	--	W31	--	V	GTAW	180	--	--	Acc
PY4-2A-4	--	W47	--	V	GTAW	358	--	--	Acc
PY4-2A-4	--	W47-1	--	V	GTAW	358	--	--	Acc
PY4-2A-4	--	W61	--	V	GTAW	358	--	--	Acc
PY4-2A-4	--	W80	--	V	GTAW	358	--	--	Acc
PY4-2A-5	--	W91	--	V	GTAW	188.5	--	--	Acc
PY4-2A-5	--	W94-1	--	V	GTAW	188.5	--	--	Acc
PY4-2A-6	--	W95	--	V	GTAW	280	--	--	Acc
PY4-2A-6	--	W96	--	V	GTAW	280	--	--	Acc

备注:热处理状态(HTS--Heat Treatment State)
Notes:缺陷性质及大小(DNS--Defect Nature and Size)

未熔合(LOF--Lack of Fusion) 未焊透(LOP--Lack of Penetration) 夹渣(S.I--Slag Inclusion)
裂纹(C--Crack) 气孔(P--Porosity) 合格(Acc--Acceptance) 不合格(Rej--Rejection)

签字 Signature	检验员(Inspector) Lin Wenzhong	技术监督(Tech. Supervisor) Tang Yuezun	签字授权人(Authorized Signee) 2018.10.23
日期 Date	2018.10.23	2018.10.23	2018.10.23

检测报告附图
SKETCH OF DETECTION POSITION

报告编号:

Report No: CJP-WR-094-022-MT001-18-062



W14-1



W22-1



W25



W30-1



W31




W47

检测报告附图
SKETCH OF DETECTION POSITION

报告编号:

Report No: CJP-WR-094-022-MT001-18-062

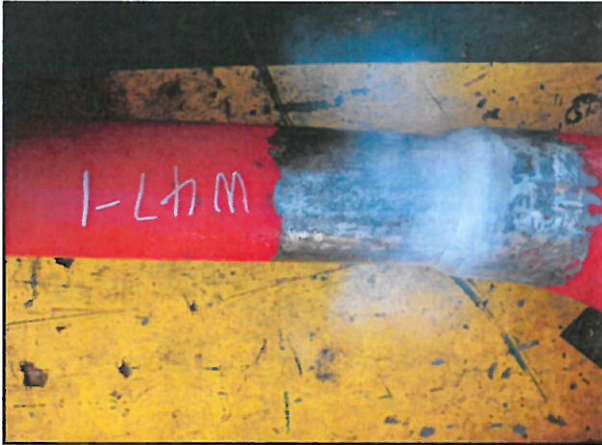

W47-1



W61



W80



W91



W94-1



W95



检测报告附图
SKETCH OF DETECTION POSITION

报告编号:

Report No: CJP-WR-094-022-MT001-18-062



W96



W97



W98



备注

Remark

1. 报告无检测单位“检测专用章”无效。
Report without the specified inspection stamp of CJP company is invalid.
2. 报告无操作人员或评片人、技术监督、技术负责人签字无效。
Report without the signatures of operator of film judge, tech. supervisor and tech. principal is invalid.
3. 本报告涂改无效。
Report with alteration will be invalid.
4. 本报告仅对被检产品受检部位负责。
Report is only responsible for the inspective pieces.
5. 未经检测单位同意不得复制本报告。
Report should not be copied without the agreement of CJP company.
6. 委托单位对检测结果若有异议，请于十五日内提出。
Client should inform CJP company within 15 days if there're any question about the inspective result.
7. 本报告一式三份；本公司存档一份，客户两份。
Report is in triplicity, original stored in CJP company, two copies for client.
8. 未加盖 CMA 章的检测报告，不具备向社会起证明作用的数据和结果。
The data and result of the inspection report that unsealed can not be proved to society.

检测单位：深圳市诚锦鹏实业有限公司

Contractor: Shenzhen Chengjinpeng Industrial Co.,LTD

地址：深圳市南山区月亮湾大道 2076 号高科大厦 6 层 C3

Address: Room C3, 6/F Gaoke Building, No.2076, Yueliangwan BLVD,
Nanshan District, Shenzhen.

电话/TEL: 0755-86274981/26440278

URL: <http://www.cjpsz.com> E-mail: cjpsz126@126.com
